Memorial Square/Meridian Place Project Update

March 23, 2017

PRESENTED BY

Gus Diamantopoulos

Facility Planning & Development



Project Update



- Goals
- How we got here
- Timelines
- Budget
- Conceptual review
- What's Next



Design that Follows Council Direction

- Cenotaph to remain in design as a focal point
- Fred Grant Street elimination
- Elimination of the definition of roads and only consider seamless roads
- Provide hard surface spaces
- Introduction of historic piece
- Include historic reference link to 9 Mile Portage
- Seamless edges Patio's/cafes along edges
- Performance Theater space
- Pedestrian access
- Linkage to kempenfelt Bay
- Amenities



Partnership and Collaboration

- Early and continuous open team approach with BIA and City
- All appropriate City Departments engaged from the project kick off
- Project Delivery Two Stage Design Build Guaranteed Maximum Price Contract awarded to Rutherford Contracting in partnership with PMA Landscape Architects



Timelines



- RFP- November
- Contract Execution January
- Stakeholder Engagement February
- 75% Design Development April
- Design Build Contract/G M P May
- Construction Start June
- Memorial Square made available for Remembrance Day
- Grand opening Spring 2018



Budget

- Original budget
- Current Budget
- DB Contract award


\$4,247,747

\$3,990,000

\$3,800,000












The City of BARRIE




Bottom of Steps - Meridian Place

Imagery of Remembrance creates a mosaic on the faces of the steps leading up towards the Cenotaph.

Central Staircase - Section 1:100



The City of BARRIE

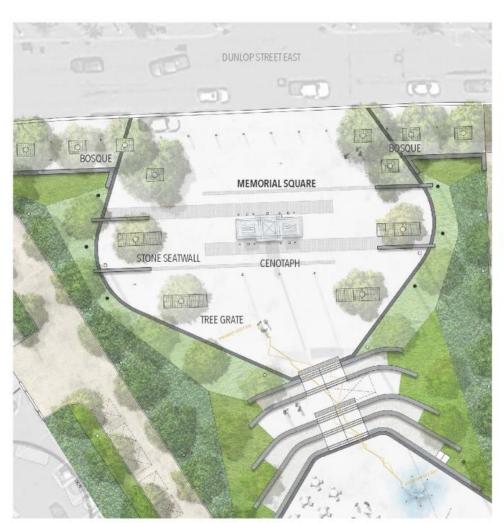

MEMORIAL SQUARE - Streetscape








MEMORIAL SQUARE - Plaza





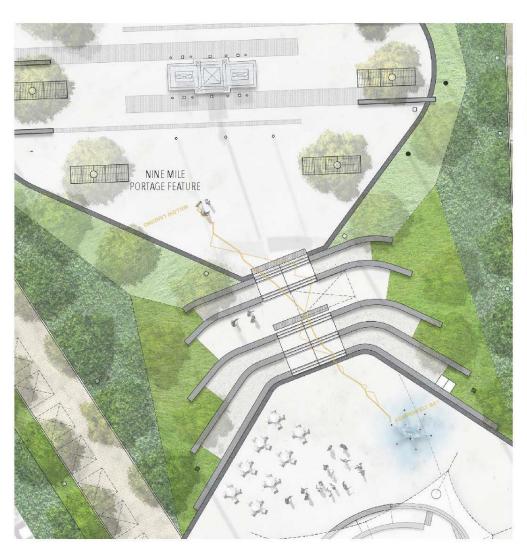

MEMORIAL SQUARE - Interpretive







MERIDIAN PLACE - Terraces





Meridian Place Concept



MERIDIAN PLACE - Stage



Meridian Place Concept



MERIDIAN PLACE - Interpretive





Meridian Place Concept



EAST PROMENADE - Patios





Memorial Square/Meridian Place



PROMENADES - Planting





What's Next?

- ACC Support
- Continued Collaboration with BIA
- Stakeholder Review and Acceptance
- Design Build Guaranteed Maximum Price Contract
- Construction
- Operational and Programing agreements
- Celebration



